


KNIFE RIVER PRODUCTION UPDATE & LOOKAHEAD



		OSU Inovation District 3 Week Sneek Peak																			
Activity	Contractor	Mon 27-Jan	Tue 28-Jan	Wed 29-Jan	Thu 30-Jan	Fri 31-Jan	Sat 1-Feb	Sun 2-Feb	Mon 3-Feb	Tue 4-Feb	Wed 5-Feb	Thu 6-Feb	Fri 7-Feb	Sat 8-Feb	Sun 9-Feb	Mon 10-Feb	Tue 11-Feb	Wed 12-Feb	Thu 13-Feb	Fri 14-Feb	Sat 15-Feb
Dywell Ex/ Construct.	KRC	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	
Lower Existing Elec. @ Cascade & 15th Sewer on 15th	KRC						X														
Sewer at 15th & Inov. North and West	KRC	X	X	X					X	X	X	X	X			X					
Cascade Ln HDPE Ground Water 15th street HDPE	KRC								X	X		X	X	X		X	X	X	X	X	

NOTES:

- HDPE pipe installation has been the talk of the week as Knife River has been working with Systems West Engineering, HHRP and OSU to finalize amendments to the grand scope of the HDPE Pipe install to commence in the coming weeks.
- Knife River has been working with PP&L to adress an existing power line at the intersection of 15th street and cascade that does not have adequate cover to comply with city of bend standards. We are in the process of coming up with a plan to lower the existing line to ensure adequate cover for future roadway.
- Next week we should expect to start finishing up some dry wells and beginning final infiltration testing with HHRP to evaluate performance and ensure OSU is receiving an adequate product for future improvments.
- Quality Drilling was on site Friday to proceed with drilling and blasting selected dry-well galleries. 2 shots occurred for a total of 6 DW galleries blasted

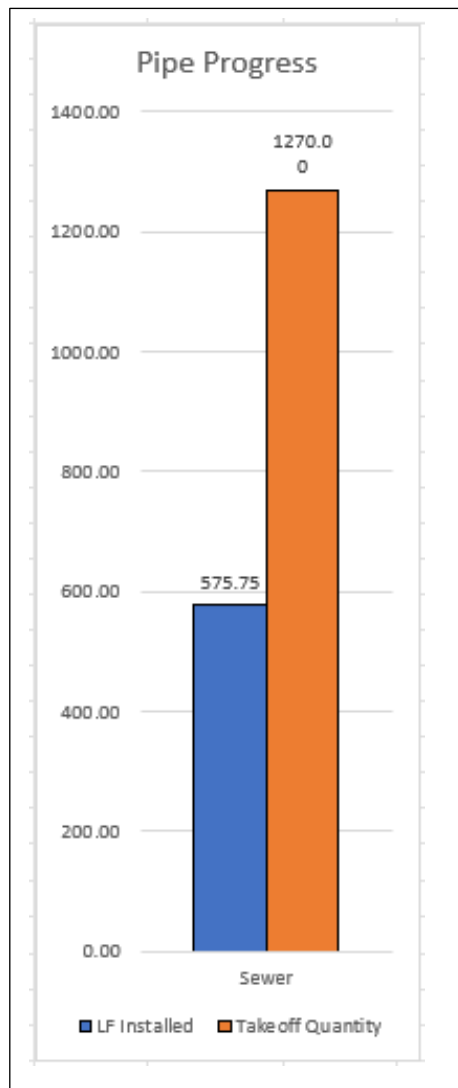

Dry-Well Progress		Drywell Checklist								
Complete	Remaining	DIG	Pre- Inf Test	Drain Rock	Set DW	Strm Pipe	Pour cap	Cap Fill	Comp. Test	Fin. Inf. Tes
	25									
		DW-1s	X	X	X	X				
		DW-2s	X	X	X	X				
		DW-3s	X	X						
		DW-4s	X	X	X	1/2				
		DW-7s	X	X	X	1/2				
		DW-8s								
		DW-9s								
		DW-10s	X	X	X	X		X		
		DW-11s	X	X	X	X		X		
		DW-12s	X	X	X	X		X		
		Sed-1								
		Sed-8								
		Sed-9								
		Sed-10								
		Sed-11								
