

# OSU-CASCADES INNOVATION DISTRICT REMEDIATION PHASE 1

## WEEKLY PROGRESS REPORT

04/21/2025 to 04/25/2025



## WEEKLY SUMMARY


HDPE pipe crew finished all HDPE pipe installation this week and pressure tested HW, CHW, CW, RW and GW systems. All passed!

Water crews continue to install ductile iron water line through the interior of the project.

Knife River grade crews began working on installing Bee-hives and interior parking lot drainage to further grade and prep the parking lot.

Knifer River continues to open dry utility trench crossings for Rosendin to install in the coming days.

## PHOTOS

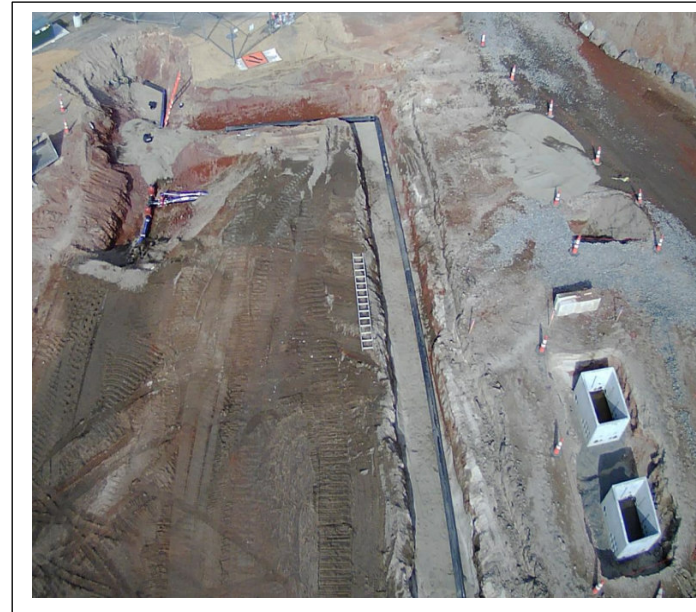

## POINTS OF EMPHASIS

- Final HDPE product
- Parking lot storm
- Water install

## UPCOMING ACTIVITIES

- Electrical and communication install
- HDPE testing
- Parking lot install

